


All performance values shown on this report are for products of a standard configuration, tested in accordance with AAMA specifications, in a laboratory environment under optimum conditions. They are provided for purposes of comparison only. Performance values will vary according to project specifications, such as but not limited to, quality installation workmanship, product size, configuration, hardware, glass type, and accessories. When field testing is required, it is recommended that all EFCO products be tested in accordance with AAMA 502-02 unless otherwise specified.



CONSTRUCTION CONSULTING LABORATORY, *INTERNATIONAL*

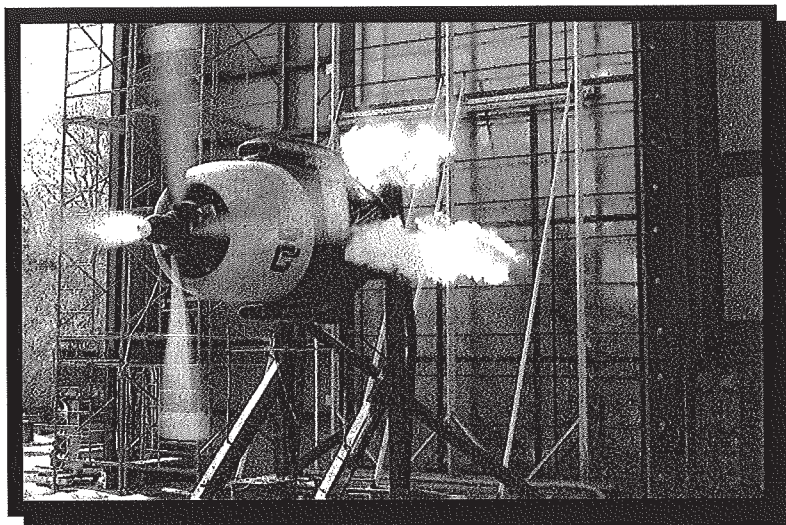

TEST REPORT:

**AAMA 501-05 Curtain Wall Mock-Up Testing
EFCO Corporation, a Pella Company
SERIES 5600 System 2 and 4 Sided
Structural Glazed Curtain Wall Mock-Up
REPORT #CCLI 12-052**

March 29, 2012

Prepared for:

EFCO Corporation, a Pella Company
1000 County Road
Monett, MO 65708

1601 Luna Road
Carrollton, Texas 75006

S-UNITED, INC.
A Quality Control Company

Office: (972) 242-0556
FAX: (972) 245-6047



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012

TABLE OF CONTENTS

1. PROJECT DATA	1
2. MOCK-UP DESCRIPTION	1
3. TEST EQUIPMENT	3
4. TESTING ALLOWABLES	4
5. TESTING SEQUENCE	5
6. TESTING and RESULTS	5
7. CONCLUSION	10

APPENDIXES

APPENDIX A: EFCO CORPORATION, A PELLA COMPANY SERIES 5600 SYSTEM 2
and 4 SIDED STRUCTURAL GLAZED CURTAIN WALL MOCK-UP
DRAWINGS

This report is not complete unless these drawings are stamped and initialed by **CCLI** as illustrated below

Sheet	Detail	Date	Stamped as Illustrated
1	Title	3/18/11	 CONSULTING LABORATORY, INTERNATIONAL 1601 Luna Road Carrollton, Texas 75006 Phone (972) 242-0556 Report # 12-052 Date 3-29-12 Reviewed BY <u>GW</u>
2	Elevation	3/18/11	
3	SSG Horizontals	3/18/11	
4	Captured Horizontals	3/18/11	
5	1/4" SSG Verticals	3/18/11	
6	1" SSG Verticals	3/18/11	
7	Anchor	3/18/11	

APPENDIX B: PHOTOGRAPHS

S-UNITED, INC.

A Quality Control Company



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012
Page 1 of 10

1. PROJECT DATA

Project: AAMA 501 Curtain Wall Mock-Up Performance Testing
EFCO Corporation, A Pella Company Series 5600 System
2 and 4 Sided Structural Glazed Curtain Wall Mock Up

Date Started: June 6, 2011
Date Completed: June 7, 2011
Tested By: Construction Consulting Laboratory, *International* in Carrollton, TX

Tested For: EFCO Corporation, A Pella Company
1000 County Road
Monett, Mo 65708

Witnessed By: (All or Partial Viewing)

EFCO Corporation, A Pella Company	Shannon Keeler	Brad Wells	
Construction Consulting Laboratory, <i>International</i>	Jeffrey Crump	Andy Wilson	
Construction Consulting Laboratory, <i>International</i>	Juvenal Azua	Edsson Alarcon	Chevis Wilson

2. MOCK-UP DESCRIPTION

PRODUCT TYPE: Aluminum Curtain Wall
SERIES/MODEL: 5600 System 2 and 4 Sided Structural Glazed Curtain Wall
Mock Up

CURTAIN WALL OVERALL: 12'-2¼" x 24'-0"
CONFIGURATION: Plan View, **Sheet 2, Appendix A**

GENERAL DESCRIPTION: The test specimen is identified as an EFCO Corporation, A Pella Company Series 5600 System 2 and 4 Sided Structural Glazed Curtain Wall Mock Up with a tested overall dimension of 12'-2¼" x 24'-0". The vertical elements of the mock-up were span mullions with splices at appropriate locations. The glazing included 1" and ¼" exterior and interior glazed lites. The curtain wall system was designed and manufactured by EFCO Corporation, A Pella Company.

CURTAIN WALL WEEP ARRANGEMENT: 1" x ³⁄₁₆" weep slots located 3½" from each end of captured glazed horizontal pressure plates. Face caps are weeped on the underside with a ⁵⁄₁₆" diameter weep hole located 2" from each end.

GLASS: Visions are 1" sealed insulating glass constructed of (2) pcs ¼" tempered with ½" airspace. Spandrel lites are ¼" monolithic tempered.



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012
Page 2 of 10

REINFORCEMENT: None.

CURTAIN WALL GLAZING: Perimeter pressure plate (part #5977) with thermal isolator (part #WV80) located at exterior of frame head with pre-set gasket (part #WEP7) and (part #WNEO) between pressure plate and main frame, mechanically fastened with #13-16 x $\frac{5}{8}$ " HW-SMS spaced on 9" centers. Pressure plate (part #5959) and thermal isolator (part #WV80) with pre-set gasket (part #WNEO), mechanically fastened to the horizontal intermediate mullions with #13-16 x $\frac{5}{8}$ " HW-SMS spaced on 9" centers. Setting block (part #HN60) located at 1" captured glazed horizontal intermediates and setting block (part #HN61) located at $\frac{1}{4}$ " monolithic captured glazed horizontal intermediates. Glazing adaptor (part #EP80) with pre-set gasket (part #WNEO) located at frame head and $\frac{1}{4}$ " horizontal intermediate infill interior of monolithic glass sealed to frame with silicone sealant. Glazing adaptor (part #6842) with pre-set gasket (part #WEP7) located at frame $\frac{1}{4}$ " horizontal intermediate infill, frame sill infill and frame jamb infills interior of monolithic glass, adapter sealed to frame and glass with silicone sealant. $\frac{1}{4}$ " adaptors attached with #6-15 x $1\frac{1}{4}$ " PL-FH-SMS. Frame sill and jambs contain perimeter trim channel (part #3726) attached to mullions with #10-15 x 1" PI-PH-SMS tek screws with perimeter trim cover set in silicone. Glazing adaptor (part #6552) with pre-set gasket (part #WEP7) located at frame $\frac{1}{4}$ " vertical intermediate infill interior of monolithic glass, adapter sealed to frame and glass with silicone and backer rod and silicone full length of verticals exterior face. 5188 setting chair (part #KW75) with setting block (part #HN91) located at quarter points with silicone at the exterior face full length of the structurally glazed horizontal intermediates.

SEALANT: Curtain wall was perimeter sealed at the head and sill with backer rod and Bondaflex silicone and the frame jambs were sealed with perimeter gasket bedded in Bondaflex silicone at chamber jamb steel and lateral edge of frame jambs. Exterior perimeter seal is set behind frame perimeter pressure plate on the frame head. Silicone sealant is applied to glazing gasket ends and all frame member ends are buttered with silicone. Glazing adaptors are sealed at the interior with Bondaflex silicone. Bondaflex silicone applied at the ends of the horizontal-to-vertical connections. Vertical glazing adapters sealed to horizontal glazing adapters.

CURTAIN WALL ANCHORAGE: Vertical mullions are anchored at frame head and sill with aluminum M and F clips which are attached to chamber steel with two (2) $\frac{3}{8}$ "-16 x $1\frac{1}{2}$ " HX-MS through bolts with flat washers and nut per clip at each vertical mull. 5" x 3" x $\frac{1}{4}$ " thick channel which is welded to chamber and anchored to intermediate vertical mullions with two (2) $\frac{3}{8}$ "-16 x $3\frac{1}{2}$ " HX-MS through bolts with flat washers and nut per clip at each vertical mull. Frame jambs are attached to 5" x 3" x $\frac{1}{4}$ " thick angle which is welded to chamber with two (2) $\frac{3}{8}$ "-16 x $3\frac{1}{2}$ " HX-MS through bolts with flat washers and nut per clip at each vertical mull.



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012
Page 3 of 10

SPLICES: Vertical members are slipped onto 4½" aluminum splices (part #KY86) with ½" joint sealed with silicone. Shear block attached to splice with #8-18 x ¾" HW-SMS.

OTHER FEATURES: Head and sill shear block (part #KY49 and KY50) attached to frame SSG vertical intermediate mullion (part #6551) with #14-10 x ½" HW-SMS screws. Horizontal intermediate mullion shear blocks (part #KW03) attached to frame vertical intermediate mullion (part #6551) with #14 - 10 x ½" HW-SMS screws. Intermediate horizontals attached to shear block above splice with #8-18 x ¾"HW-SMS.

3. TEST EQUIPMENT

- 3.1 Test chamber consisted of structural steel beams, columns, and bulkheads and were accessible through bulkhead doors.
- 3.2 Pressure differentials were created with reversible pumps for positive/negative loading.
- 3.3 Pressure differentials between the specimen interior and the atmosphere were measured with manometers.
- 3.4 Air infiltration was measured with a Meriam laminar flow element and inclined manometers. Chamber pressure was measured with a Dwyer inclined manometer.
- 3.5 Water was applied to the specimen from a spray rack equipped with swirl-type nozzles spaced two feet on center in vertical and horizontal directions, which under controlled pressure delivered a minimum of five gallons per square foot per hour on the specimen.
- 3.6 Dynamic winds were generated by a Curtiss Wright 3350 Radial Aircraft Engine with a four (4) bladed propeller, 13'-6" diameter, which generates typical and atypical wind conditions.
- 3.7 Structural variations were measured with dial indicator gauges with maximum movement hands located throughout the test specimen.



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012
Page 4 of 10

4. TESTING ALLOWABLES

- 4.1 **AIR INFILTRATION:** Total amount of air infiltration shall not exceed **.06 CFM** per square foot (psf) of the exterior wall tested.

MAXIMUM ALLOWABLE

Mock-Up System #1: $12'-2\frac{1}{4}" \times 24'-0" = 292.5 \text{ ft}^2 \times .06 = 17.55 \text{ total CFM}$.

- 4.2 **STATIC WATER PENETRATION:** There shall be no uncontrolled water penetration during or at the conclusion of this test at the static pressure of 15 psf.

Note: "Uncontrolled water" is defined as any water that appears on any normally exposed interior surfaces, that is not contained or drained back to the exterior, or that can cause damage to adjacent materials or finishes. Water contained within drained flashings, gutters, and sills is not considered water leakage. The collection of up to one half ($\frac{1}{2}$) ounce of water (14.8 cc) in a fifteen (15) minute test period on top of any interior stop or stool integral with the wall system shall not be considered water leakage.

- 4.3 **DYNAMIC WATER PENETRATION:** There shall be no uncontrolled water penetration during or at the conclusion of this test at the slipstream velocity of 76 mph.

- 4.4 **DESIGN LOAD DEFLECTIONS:** There shall be no system failure and deflection of aluminum members at 100% of design load and shall not exceed L/175.

Vertical Span (L): $11'-11\frac{7}{8}"$ or 143.85	Horizontal Span (L): $45.75"/175$
Vertical Span Allowable = 0.822"	Horizontal Span Allowable = 0.261"

- 4.5 **Intermediate Lateral Displacement:** Design Displacement, shift intermediate support beam $0.010 \times$ longest vertical anchor spacing. $0.010 \times 12'-0" = 1.44"$. Specimen must pass air infiltration and static water resistance testing with the same allowable noted in 4.1 and 4.2.

- 4.6 **PROOF LOAD RESIDUAL:** The permanent deformation of the aluminum members shall not exceed 2% of span at 150% of design load.

Vertical Span (L): $143.85 / 500"$	Horizontal Span (L): $45.75 / 500"$
Vertical Span Allowable = .288"	Horizontal Span Allowable = 0.091"

- 4.7 **Intermediate Lateral Displacement:** Proof Displacement, shift Intermediate support beam $0.015 \times$ longest vertical anchor spacing. $0.015 \times 12'-0" = 2.16"$. Report any damage to the specimen and/or any glass breakage.

- 4.8 **Intermediate Lateral Displacement:** Fall-out, shift Intermediate support beam $0.025 \times$ longest vertical anchor spacing. $0.025 \times 12'-0" = 3.6"$. Report any damage to the specimen and/or any glass breakage.



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012
Page 5 of 10

5. TESTING SEQUENCE

As used throughout this report, positive pressure applied to the test specimen is considered to be **inward** acting and negative pressure is considered to be **outward** acting. All location references or comments are as viewing the test specimen from the interior (room side) of the test chamber and wall system.

Positive Design Load = +70 psf Negative Design Load = -70 psf

	Series 5600 System Curtain Wall Exterior/Interior Glazed	TEST STANDARD
1	Pre Load Positive 35 psf	ASTM E 330-02
2	Static Pressure Air Infiltration Test @ 6.24 psf	ASTM E 283-04
3	Static Pressure Water Penetration Test @ 15 psf	ASTM E 331-00
4	Dynamic Water Penetration @ 76 mph (approximate 15.0 psf)	AAMA 501.1-05
5	Structural Load by Static Pressure Test @ 50% & 100% of Design Loads	ASTM E 330-02
6	Static Pressure Air Infiltration Test @ 6.24 psf	ASTM E 283-04
7	Static Pressure Water Penetration Test @ 15 psf	ASTM E 331-00
8	Intermediate Lateral Design Displacement (0.010 x 144 = 1.44")	AAMA 501.4-00
9	Static Pressure Air Infiltration Test @ 6.24 psf	ASTM E 283-04
10	Static Pressure Water Penetration Test @ 15 psf	ASTM E 331-00
11	Structural Load by Static Pressure Test @ 150% of Design Load	ASTM E 330-02
12	Intermediate Lateral Proof Displacement (0.015 x 144 = 2.16")	AAMA 501.4-00
13	Intermediate Lateral Fall Out Displacement (0.025 x 144 = 3.60")	AAMA 501.4-00

6. TESTING and RESULTS

6.1 Preload Positive Pressure in accordance with ASTM E 330-02 and job specifications.

Subject the test specimen to a static pressure differential of **35 psf**. This load was maintained for 10 seconds and released. An inspection was made to determine if any failure occurred.

Results: No visible differences were observed within the specimen or test chamber.

6.2 Static Pressure Air Infiltration Test @ 6.24 psf per ASTM E 283-04

The specimen and perimeter sealant joints were completely covered with an impervious 4 mm plastic material and duct tape, thus allowing no movement of air through the specimen. The exterior face of the specimen was subjected to a positive pressure differential of 6.24 psf to obtain a leakage rate for the test chamber. The plastic bag was removed and the chamber infiltration was subtracted from the total air infiltration resulting in the infiltration rate of the test specimen, **Photograph 1, Appendix B.**



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012
Page 6 of 10

MAXIMUM ALLOWABLE

Mock-Up System #1: $12'-2\frac{1}{4}" \times 24'-0" = 292.5 \text{ ft}^2 \times .06 = 17.55 \text{ total CFM}$.

Results: Passed

Chamber	Specimen+Chamber	Cfm/Ft ²	Total Infiltration	Total CFM Allowable
29.56 Cfm ²	30.57 Cfm	.003 Cfm/Ft ²	1.00 Cfm	17.55 Cfm ²

6.3 Static Pressure Water Penetration Test @ 15 psf per ASTM E 331-00

Water was applied to the exterior face of the specimen at a minimum rate of five (5) gallons per square foot per hour of wall area, in such a way as to continuously and completely cover the exterior face of the specimen. Simultaneously, a positive **inward** differential static pressure of **15 psf** was applied against the face. The application of pressure and water was maintained for a period of fifteen (15) minutes, with observers inside the chamber checking for water penetration.

Results: Passed with no water penetration observed.

Dynamic Water Penetration @ 76 mph Slipstream Velocity per AAMA 501.1-05

Water was applied to the exterior face of the specimen at a minimum rate of five (5) gallons per square foot per hour of wall area, in such a way as to completely and continuously covers the face of the specimen. Simultaneously, the wall was subjected to sufficient airflow from an aircraft engine with a four-bladed propeller, approximately 13'-6" in diameter, approximately 20' in front of the specimen. The application of airflow and water was maintained for a period of fifteen (15) minutes, with observers inside the chamber checking for water penetration, **Photograph 2, Appendix B**.

Results: Passed with no water penetration observed.

6.4 Uniform Structural Load @ 50% & 100% of Design Loads per ASTM E 330-02

Dial indicators were installed to measure deflection and residuals at ends and midspan of typical horizontal and vertical members.

Test: With the specimen set in a positive mode, all indicators were set on zero. A positive pressure of **35 psf (inward)** equal to 50% of the design load was applied and held for ten (10) seconds, then released. The indicators were read and the data was recorded. At the conclusion of the 50% test load, a positive pressure of **70 psf (inward)** equal to 100% of the design load was applied and held for ten (10) seconds, then released.

Allowable: Vertical Span Allowable = 0.822" Horizontal Span Allowable = .261"

Indicator Location	Bottom or Right	Midspan	Top or Left
Vertical Mullion	Ind. No 1	Ind. No 4	Ind. No 5
Splice	Ind. No 2		Ind. No 3
Horizontal Vision	Ind. No 6	Ind. No 7	Ind. No 8



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012
Page 7 of 10

Results: Passed with all net deflections below the allowable.

POSITIVE STRUCTURAL DEFLECTION TABLE							
Indicator #	50% Design Load 35 Psf			100% Design Load 70 Psf			
	Total	Residual	Deflection	Total	Residual	Deflection	Allowable
1	.00	.00		.00	.00		
2	.09	.00		.40	.01		
3	.10	.00		.45	.01		
4	.25	.00	.225	.85	.01	.775	.822
5	.05	.00		.15	.01		
6	.00	.00		.05	.00		
7	.00	.00	.00	.02	.00	.005	.261
8	.00	.00		.00	.00		

The vacuum/blower pumps were reversed and set to perform in a negative mode. The test specimen was subjected to a negative pressure of **-35 psf (outward)** equal to 50% of design load to set the specimen in a negative mode. The pressure was held for ten (10) seconds and released.

Test: With the specimen set in a negative mode, all indicators were set on zero. A negative pressure of **-35 psf (outward)** equal to 50% of the design load was applied and held for ten (10) seconds, then released. The indicators were read and the data was recorded. At the conclusion of the 50% test load, a negative pressure of **-70 psf (outward)** equal to 100% of the design load was applied and held for ten (10) seconds, then released.

Results: Passed with all net deflections below the allowable.

NEGATIVE STRUCTURAL DEFLECTION TABLE							
Indicator #	50% Design Load 35 Psf			100% Design Load 70 Psf			
	Total	Residual	Deflection	Total	Residual	Deflection	Allowable
1	.00	.00		.02	.00		
2	.13	.00		.11	.01		
3	.14	.00		.25	.02		
4	.30	.00	.260	.85	.08	.750	.822
5	.08	.00		.18	.01		
6	.00	.00		.05	.00		
7	.00	.00	.00	.02	.00	.005	.261
8	.00	.00		.00	.00		



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012
Page 8 of 10

6.6 Static Pressure Air Infiltration Test @ 6.24 psf per ASTM E 283-04

The exterior face of the specimen was again subjected to a positive pressure differential of 6.24 psf to obtain a total leakage rate for the test chamber and the specimen.

MAXIMUM ALLOWABLE

Mock-Up System #1: $12'-2\frac{1}{4}" \times 24'-0" = 292.5 \text{ ft}^2 \times .06 = 17.55 \text{ total CFM}$.

Results: Passed

Chamber	Specimen+Chamber	Cfm/Ft ²	Total Infiltration	Total CFM Allowable
28.06 Cfm ²	31.07 Cfm	.003 Cfm/Ft ²	1.50Cfm	17.55 Cfm ²

Note: Reduction of total CFM attributed to wet chamber closures reducing overall chamber air infiltration.

6.7 Static Pressure Water Penetration Test @ 15.0 psf per ASTM E 331-00

Water was applied to the exterior face of the specimen at a minimum rate of five (5) gallons per square foot per hour of wall area, in such a way as to completely and continuously cover the face of the specimen. Simultaneously, a positive **inward** differential static pressure of **15 psf** was applied against the face. The application of pressure and water was maintained for a period of fifteen (15) minutes, with observers inside the chamber checking for water penetration.

Results: Passed with no water penetration observed.

6.8 Seismic Induced Interstory Drift Test Design Displacement @ 0.010 x Story Height per AAMA 501.4-00

The intermediate chamber beam was subjected three (3) shifting cycles. One (1) cycle consist of a lateral shift from start point 0" to 1.44" towards the left back to start point 0" and towards the right to 1.44". Shift duration was 60 seconds with the specimen left in the full shifted position for a minimum of 10 seconds before being returned to the start point.

Results: Passed with no glass breakage.



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012
Page 9 of 10

6.8 Static Pressure Air Infiltration Test @ 6.24 psf per ASTM E 283-04

The exterior face of the specimen was again subjected to a positive pressure differential of 6.24 psf to obtain a total leakage rate for the test chamber and the specimen.

MAXIMUM ALLOWABLE

Mock-Up System #1: 12'-2¼" x 24'-0" = 292.5 ft² x .06 = 17.55 total CFM.

Results: Passed

Chamber	Specimen+Chamber	Cfm/Ft²	Total Infiltration	Total CFM Allowable
28.06 Cfm²	32.07 Cfm	.008 Cfm/Ft²	2.50 Cfm	17.55 Cfm²

6.9 Static Pressure Water Penetration Test @ 15 psf per ASTM E 331-00

A positive **inward** differential static pressure of **15 psf** was applied against the face. The application of pressure and water was maintained for a period of fifteen (15) minutes, with observers inside the chamber checking for water penetration.

Results: Passed with no water penetration observed.

6.10 Uniform Structural Load @ 150% of Design Loads per ASTM E 330-02

Vertical Span Allowable = .822" Horizontal Span Allowable = .261"

Test: With the specimen set in a positive mode, midspan indicators were set on zero. A positive pressure of **105 psf (inward)** equal to 150% of the design load was applied and held for ten (10) seconds, then released.

Test: With the specimen set in a negative mode, midspan indicators were set on zero. A negative pressure of **105 psf (outward)** equal to 150% of the design load was applied and held for ten (10) seconds, then released. The indicators were read and the data was recorded.

Maximum permanent set recorded during positive loading

Results: SSG Vertical Mullion Permanent set: .045 **Allowable:** .288"

Results: Spandrel Horizontal Permanent set: 0.00 **Allowable:** .091"

Maximum permanent set recorded during negative loading

Results: SSG Vertical Mullion Permanent set: .130 **Allowable:** .288"

Results: Spandrel Horizontal Permanent set: 0.04 **Allowable:** .091"



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012
Page 10 of 10

6.11 Seismic Induced Interstory Drift Test Proof Displacement @ 0.015 x Story Height per AAMA 501.4-00

The intermediate chamber beam was subjected three (3) shifting cycles. One (1) cycle consist of a lateral shift from start point 0" to 2.16" towards the left back to start point 0" and towards the right to 2.16". Shift duration was 60 seconds with the specimen left in the full shifted position for a minimum of 10 seconds before being returned to the start point, **Photograph 3, Appendix B.**

Results: Passed with no glass breakage.

6.12 Seismic Induced Interstory Drift Test Fall-Out Displacement @ 0.025 x Story Height per AAMA 501.4-00

The intermediate chamber beam was subjected three (3) shifting cycles. One (1) cycle consist of a lateral shift from start point 0" to 3.60" towards the left back to start point 0" and towards the right to 3.60". Shift duration was 60 seconds with the specimen left in the full shifted position for a minimum of 10 seconds before being returned to the start point.


Results: Passed with no glass breakage.


7. CONCLUSION

The tested specimen EFCO Corporation, A Pella Company Series 5600 System 2 and 4 Sided Structural Glazed Curtain Wall Mock Up performed within the specified criteria.

Respectfully submitted,

CONSTRUCTION CONSULTING LABORATORY, *INTERNATIONAL*


JEFFREY CRUMP
TESTING MANAGER


WESLEY WILSON
LABORATORY MANAGER



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012

APPENDIX A

EFCO CORPORATION, A PELLA COMPANY SERIES 5600 SYSTEM 2 AND 4 SIDED STRUCTURAL GLAZED CURTAIN WALL MOCK-UP DRAWINGS

Sheet	Detail	Date
1	Title	3/18/11
2	Elevation	3/18/11
3	SSG Horizontals	3/18/11
4	Captured Horizontals	3/18/11
5	1/4" SSG Verticals	3/18/11
6	1" SSG Verticals	3/18/11
7	Anchor	3/18/11

SERIES 5600 SYSTEM 2 AND 4 SIDED STRUCTURAL GLAZED CURTAIN WALL MOCK-UP

ERASE NOTE FOR
LAB COPY

DESIGN TEST CRITERIA

D.P. = 50 PSF
DEFLECTION = $L/175$
ALLOWABLE OF 42 INCHES
WATER = 15 LB

**CONSTRUCTION CONSULTING
& LABORATORY INTERNATIONAL**
1601 Luna Road
Carrollton, Texas 75006
Phone (972) 242-0556

TEST NO: XX-XXXX

DRAWN BY	TK	CHECKED BY	SCALE	REV.
DATE	3-18-11	DATE	HALF	




EFCO CORPORATION
1000 County Road 4, Brentwood, Missouri 63026

5600 SSG A.W.S.


©2011 EFCO CORPORATION ALL RIGHTS RESERVED
REPORT # XXXX-XXX-XX

1 of 7


NOTE:
FABRICATOR AND/OR ERECTOR, THIS MOCK-UP IS TO BE FABRICATED AND SEALED AS NOTED PER GENERAL INSTALLATION INSTRUCTIONS AS NOTED IN PART #Y002.

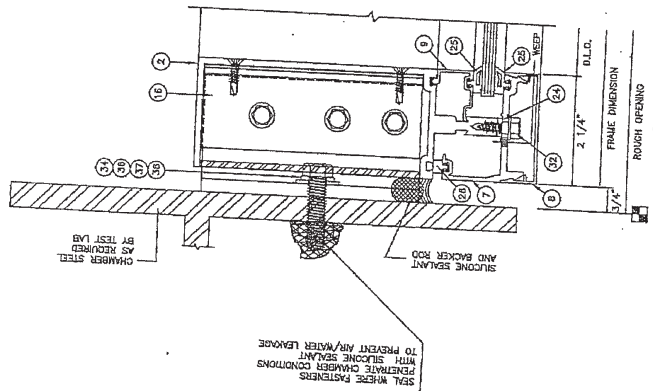

6 7" HORIZ. HEAD 1/4" INFILL



5 7" HORIZ. INTER. 1" & 1/4" INFILL




4 7" HORIZ. INTER. 1/4" & 1" INFILL

CONSULTING
LABORATORY
160
Carroll
Phone 2-2-0686


DRAWN BY	TK	CHECKED BY	SCALE	HALF	REV.	DATE	3-18-11
EFCO CORPORATION				5600 SSG A.W.S.		DATE EFCO CORPORATION ALL RIGHTS RESERVED	
1000 County Road - Mount, Missouri 65708				REPORT#		XXXX-XXX-XX	
SHEET				4 of 7			

ENLARGED DETAIL



FABRICATOR AND OR ERECTOR, THIS MOCK-UP IS TO BE FABRICATED AND SEALED AS NOTED PER GENERAL INSTALLATION INSTRUCTIONS FOR S5600 EXTERIOR GLAZED CURTAIN WALL. AS NOTED IN PART #K302.

NOTE:
EXTREME CARE MUST BE EXERCISED TO ENSURE ALL
VOIDS AT SSG JOINTS ARE COMPLETELY FILLED AND
PROPERLY TOOLED WITH NO AIR POCKETS OR GAPS IN
SEALANT JOINT.

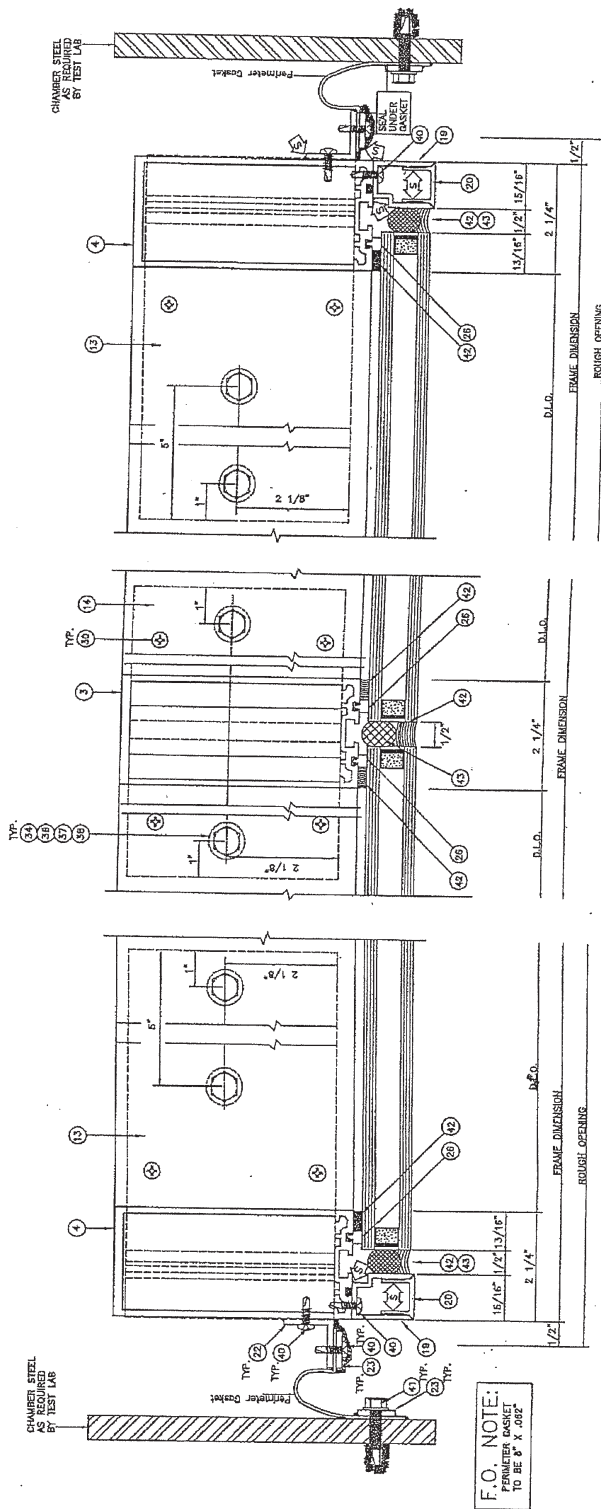

10	7" JAMB VERTICAL
	1" INFILL

11	7" INTER. VERTICAL
	1" INTER.

12'	7" JAMB VERTICAL
-----	------------------

9350-215
9002-200
P.O. Box
TWOHART
GUILFORD, N.C.

C. 100-100
 C. 100-100
 C. 100-100
 C. 100-100

DRAWN BY	TK	CHECKED BY	SCALE	REV.
DATE	3-18-11	DATE	HALF	




EFCO CORPORATION
1000 County Road • Monett, Missouri 65708

5600 SSC AWC

©2011 EFCC CORPORATION ALL RIGHTS RESERVED

NOTE:
FABRICATOR AND OR ERECTOR, THIS WORK-UP
IS TO BE FABRICATED AND SEALED AS NOTED
FOR SESSO EXTENSION CURTAIN WALL
AS NOTED IN PART #302.

NOTE:
EXTREME CARE MUST BE EXERCISED TO ENSURE ALL
JOINTS AT SSG JOINTS ARE COMPLETELY FILLED AND
PROPERLY COULDED WITH NO AIR POCKETS OR GAPS IN
SEALANT JOINT.

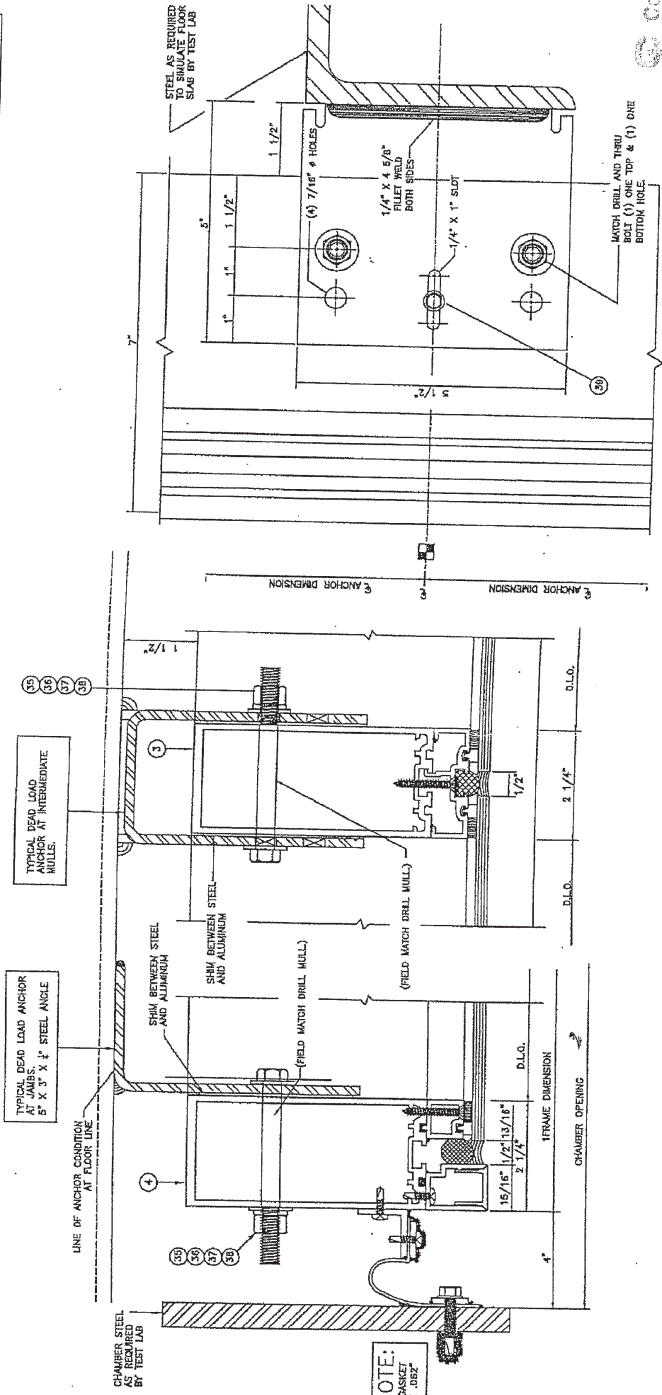

13 7" JAMB VERTICAL
1/4" INFILL W/ ANCHOR

14 7" INTER. VERTICAL
1/4" INFILL W/ ANCHOR

15 SPANDREL ANCHOR
DEAD LOAD (FIXED)

CONSTRUCTION CONSULTING
LABORATORY
1001 East 10th St
Canton, OH 44703
Phone: 330-220-0000

DRAWN BY	TK	CHECKED BY	SCALE	REV.	DATE	3-18-11
DATE	3-18-11	DATE	HALF			
EFCO CORPORATION 1000 County Road - Mount, Missouri 63078						5600 SSG A.W.S.
©2011 EFCO CORPORATION ALL RIGHTS RESERVED						REPORT # XXXX-XXX-XX
						SHEET 7 of 7

FO. NOTE:
PERMITTER QUALITY
TO BE 6" X 1/2"



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012


APPENDIX B

PHOTOGRAPHS



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012

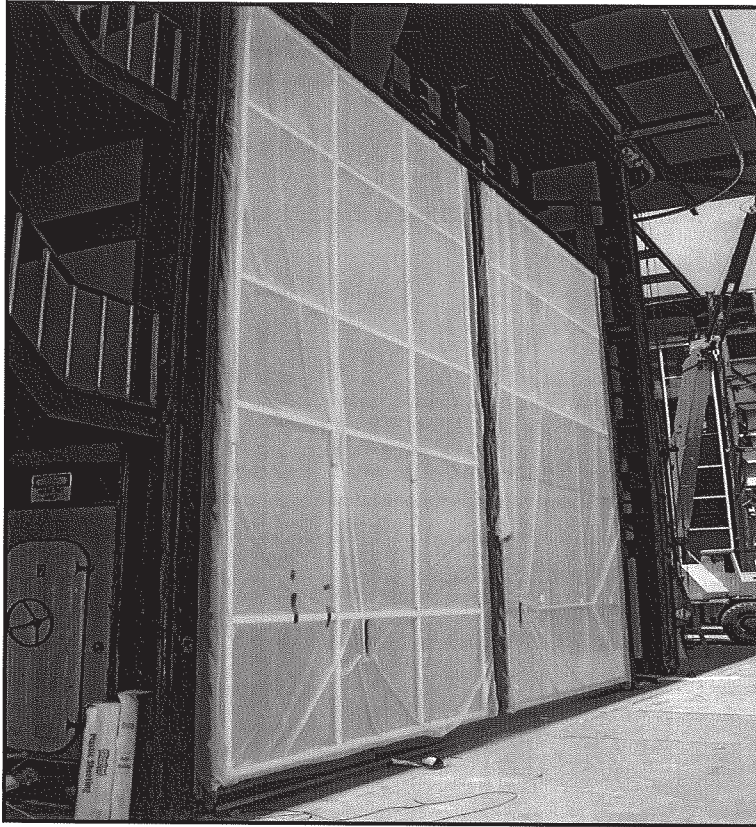

PHOTOGRAPH 1

Static Pressure Air Infiltration Test @ 6.24 psf per ASTM E 283-04

The specimen and perimeter sealant joints were completely covered with an impervious 4 mm plastic material and duct tape, thus allowing no movement of air through the specimen. The exterior face of the specimen was subjected to a positive pressure differential of 6.24 psf to obtain a leakage rate for the test chamber. The plastic bag was removed and the chamber infiltration was subtracted from the total air infiltration resulting in the infiltration rate of the test specimen.

MAXIMUM ALLOWABLE

Mock-Up System #1: $12'-2\frac{1}{4}" \times 24'-0" = 292.5 \text{ ft}^2 \times .06 = 17.55 \text{ total CFM}$.


Results: Passed

Chamber	Specimen+Chamber	Cfm/Ft ²	Total Infiltration	Total CFM Allowable
29.56 Cfm ²	30.57 Cfm	.003 Cfm/Ft ²	1.00 Cfm	17.55 Cfm ²



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012

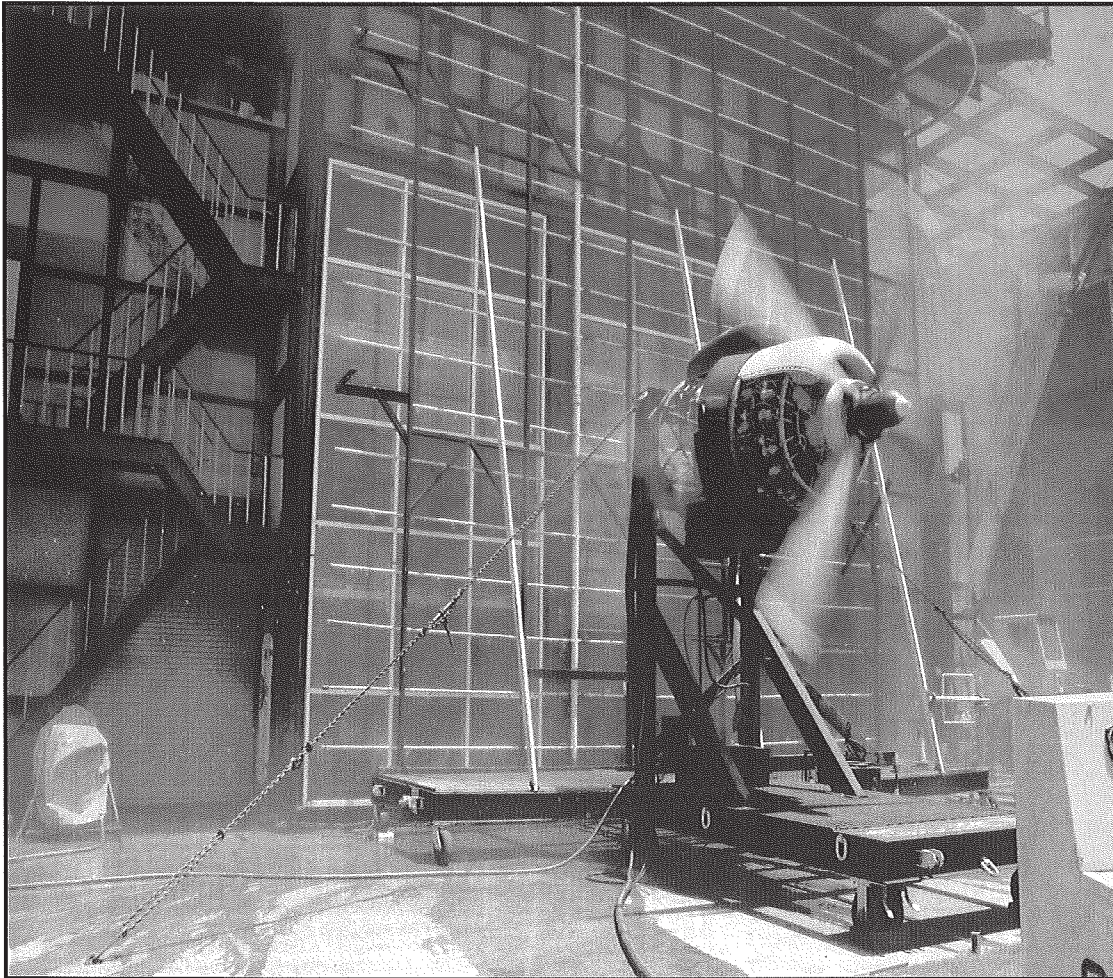

PHOTOGRAPH 2

Dynamic Water Penetration @ 76 mph Slipstream Velocity per AAMA 501.1-05

Water was applied to the exterior face of the specimen at a minimum rate of five (5) gallons per square foot per hour of wall area, in such a way as to completely and continuously covers the face of the specimen. Simultaneously, the wall was subjected to sufficient airflow from an aircraft engine with a four-bladed propeller, approximately 13'-6" in diameter, approximately 20' in front of the specimen. The application of airflow and water was maintained for a period of fifteen (15) minutes, with observers inside the chamber checking for water penetration.

Results: Passed with no water penetration observed.



AAMA 501-05 CURTAIN WALL MOCK-UP TESTING
EFCO CORPORATION, A PELLA COMPANY
SERIES 5600 SYSTEM 2 AND 4 SIDED
STRUCTURAL GLAZED CURTAIN WALL MOCK UP
REPORT CCLI #12-052

March 29, 2012



PHOTOGRAPH 3

Seismic Induced Interstory Drift Test Design Displacement @ $0.015 \times$ Story Height per AAMA 501.4-00

The intermediate chamber beam was subjected three (3) shifting cycles. One (1) cycle consisted of a lateral shift from start point 0" to 2.16" towards the left back to start point 0" and towards the right to 2.16". Shift duration was 60 seconds with the specimen left in the full shifted position for a minimum of 10 seconds before being returned to the start point.

Results: Passed with no glass breakage.

- END OF REPORT -
